


Port of Melbourne - Dredging Program 2019

ID	Task Mode	Task Name	Duration	Start	Finish	August	September	October	November	December	January	February	March	April	May	June	July
						13/08	27/08	04/09	10/09	17/09	24/09	01/10	08/10	15/10	22/10	29/10	05/11
1	↓	PoM Dredging Program Preliminaries	37.75 days	Fri 5/10/18	Mon 12/11/18												
7	↓	Compliance Requirements	271 days	Sat 15/09/18	Thu 13/06/19												
15	↓	Dredging Program	208 days	Mon 17/09/18	Sat 13/04/19												
16	📌	Boskalis Mobilisation	28 days	Mon 17/09/18	Mon 15/10/18												
17	↓	Toll Dredging	117 days	Mon 15/10/18	Sat 9/02/19												
18	📌	Mobilisation of drum cutter	60 days	Mon 15/10/18	Fri 14/12/18												
19	📌	Toll Dredging works	4 days	Mon 3/12/18	Fri 7/12/18												
20	📌	Toll Drum Cutting Operation	59 days	Wed 12/12/18	Sat 9/02/19												
21	↓	Dredging Port of Melbourne	63 days	Sat 9/02/19	Sat 13/04/19												
22	↓	POM scope of works	57 days	Sat 9/02/19	Sun 7/04/19												
23	↓	Dredging works 27/28 South Wharf (Melb Cement)	3 days	Sun 7/04/19	Wed 10/04/19												
24	↓	Sweeping	14 days	Sat 30/03/19	Sat 13/04/19												
25	↓	Practical completion - operational	0 days	Sat 13/04/19	Sat 13/04/19												

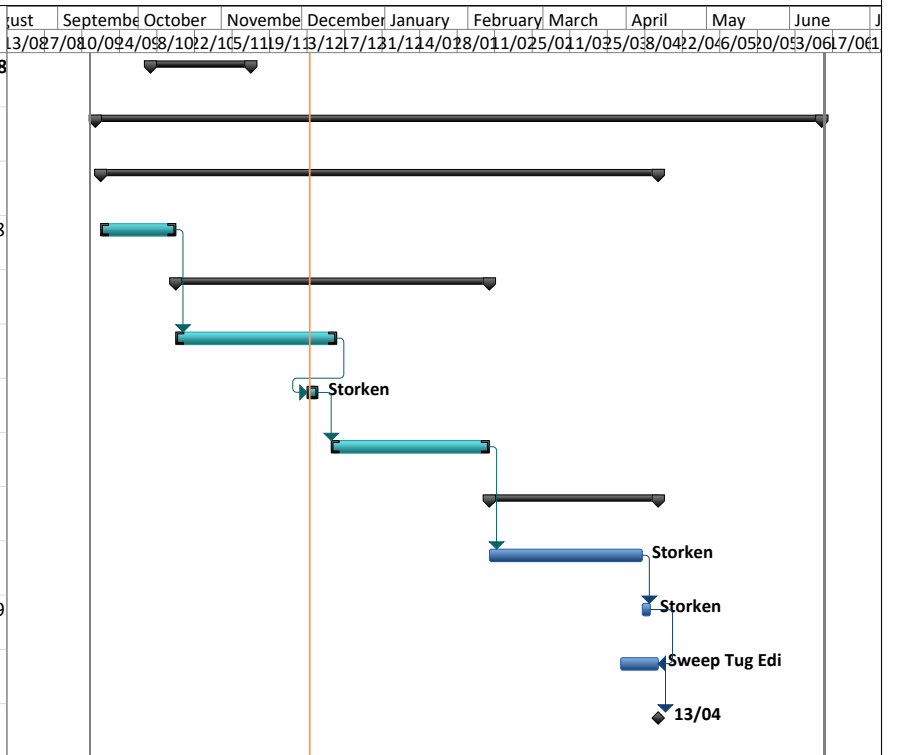

Project: DP2019 Schedule of Work Date: Tue 4/12/18	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			
